

Project Portfolio Dashboard Report

Assess portfolio health, budget signals, delivery exposure, and the data checks needed before decisions.

75

projects in portfolio

21

on hold or delayed

102.1%

reported budget utilization

Decision frame: separate what the dashboard shows from what it suggests, then validate the figures before governance action.

Delivery exposure is concentrated in the active and stalled portfolio

Active work is substantial, but the portfolio also carries a meaningful recovery queue. Nearly three in ten projects need a clear recovery, pause, or closure decision.

Status	Projects	Read-through
Active	37	Largest operating load
On hold	15	Requires pause or restart decision
Delayed	6	Requires recovery path
Planning	9	Future pipeline
Completed	8	Closed delivery record

Portfolio view · 75 projects total; average project age is 2.4 years.

21

on hold + delayed

Management implication. Review the 21 projects as a named decision queue, with recovery, pause, or closure as the explicit outcome for each.

High-priority work and two locations account for much of the load

Review capacity and dependencies where volume is highest, while protecting delivery attention for the 37 high-priority projects.

PRIORITY MIX

37

High priority

30 medium · 8 low

High-priority work is about half of the portfolio.

LOCATION LOAD

30

Mumbai + Nashik

18 Mumbai · 12 Nashik

Together, these locations represent 30 of 75 projects.

LARGEST CATEGORIES

16

Operations


15 Marketing · 14 R&D

Three categories carry the largest visible concentrations.

	Lens	Observed load	Action suggested by the pattern
	Priority	37 high	Protect staffing and dependency review
	Location	30 in Mumbai and Nashik	Focus local review capacity
	Category	Operations, Marketing, R&D	Check cross-project dependencies

Budget utilization is above plan, but the cost trend needs reconciliation

The dashboard reports actual cost of ₹3,557K and utilization of 102.1%. That is above the stated budget baseline, but the underlying monthly and departmental views are not yet reliable enough for variance decisions.

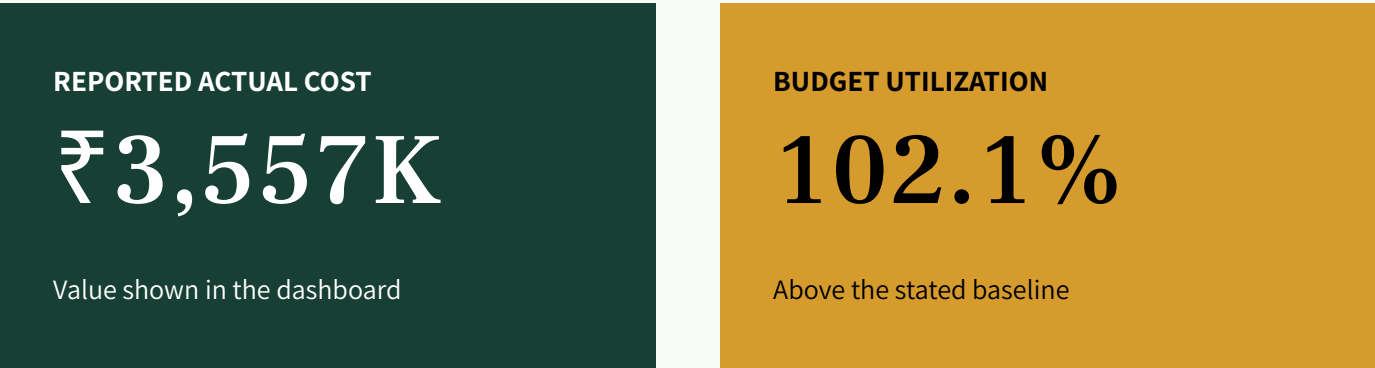

Dashboard element	Decision status
Actual-cost KPI	Use as the reported reference point: ₹3,557K.
Monthly actual-cost chart	Hold for reconciliation. At least one visible data label appears inconsistent with the plotted scale.
Department chart	Hold for comparison. The paired bars have no named series.

Control point. Reconcile monthly costs to the KPI and confirm the budget baseline and period before using the trend to assign variance ownership.

Validate the figures, then assign owners to the recovery work

The next governance cycle should resolve data reliability and delivery ownership in parallel. Each action below should end with a named owner, a decision date, and an auditable update.

01 Reconcile the cost base

Match monthly costs to the ₹3,557K actual-cost KPI, then confirm the budget baseline and reporting period.

02 Assign the stalled-work queue

Review all 21 on-hold or delayed projects. Give each a named owner, next decision date, and recovery or closure path.

03 Protect priority delivery

Check staffing and dependencies across the 37 high-priority projects, with focused reviews for Mumbai and Nashik.

04 Repair dashboard evidence

Label the two department-chart series and add an as-of date before the dashboard supports governance decisions.

DECISION STANDARD

Use the dashboard for action only after the figures are traceable and every recovery item has an owner.
